


Lab 2: Agile Backlog Creation & Sprint Simulation


Project: Blood Bank Inventory & Emergency Donor Matcher | SRN: PES1UG24CS012

Abhay Balakrishna Doddaballapur


1. Jira Backlog & Story Point Assignments

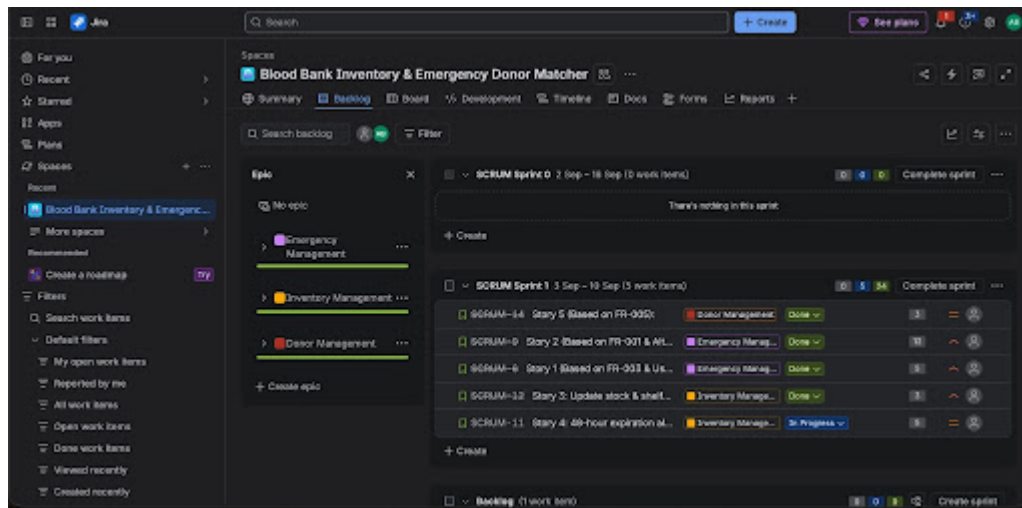

2. Sprint Board (Active Sprint View)

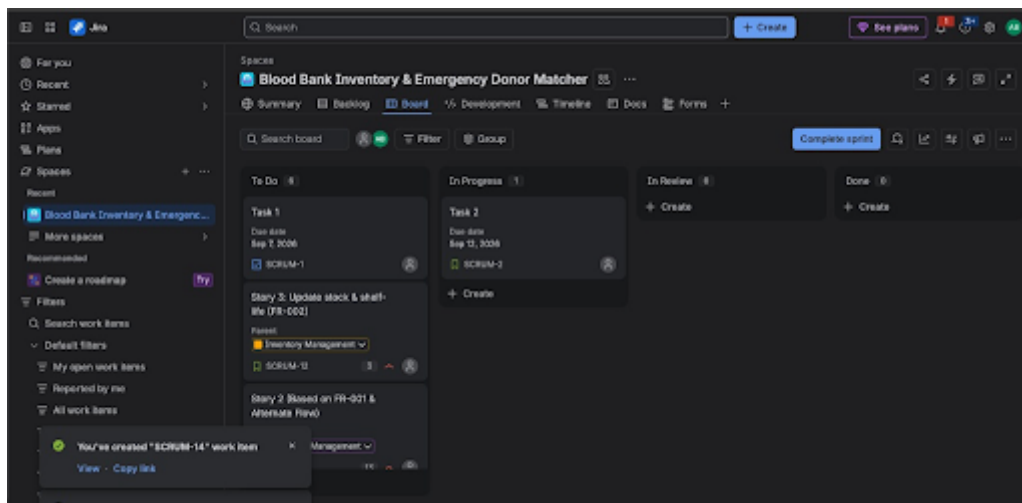

3. Burndown Chart

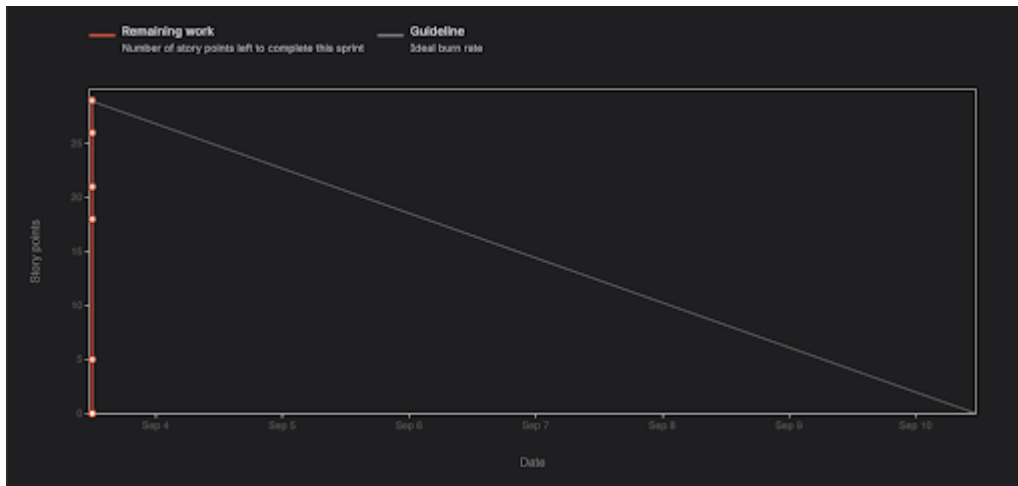

4. Reflection Questions

1. Did your estimations reflect the actual effort?

In a real-world development environment, estimating the geo-targeted SMS broadcast at 13 points reflects the high complexity of handling external APIs and location radius logic. However, because this was a simulated sprint completed in a single laboratory session, the physical effort (moving Jira cards) did not align with the estimated Fibonacci points, as all tasks took roughly the same amount of time to process on the board.

2. Was your backlog well-prioritized?

Yes, the backlog was structured logically based on business value and immediate end-user needs. Critical core functions, such as submitting an emergency request (FR-003) and broadcasting the SMS alerts (FR-001), were assigned High priority. Supporting features, like the 48-hour expiration alert and donor profile registration, were correctly categorized as Medium priority and placed lower in the backlog.

3. How did your simulated sprint align with your plan?

The simulation aligned with the overall goal, as all 29 planned story points were successfully moved from "To Do" to "Done" within the defined 1-week sprint timeframe. However, the pacing did not align with a

standard Agile workflow; instead of pacing the work over 7 days, the entire workload was processed immediately for the sake of the lab exercise.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart displayed a steep, vertical drop to zero on the very first day, rather than a gradual descent along the gray ideal burn rate guideline. While expected for a 60-minute lab simulation, in a real Agile environment, this sharp drop would indicate that the team either vastly overestimated the complexity of the sprint, or they failed to track their daily progress accurately, pushing all tickets to "Done" at the exact same time.
